



Daily Log: Tuesday 6/10/2025



Daily Log Completed
The Daily Log was completed by Ray Hutsel on Tue, Jun 10, 2025 at 06:07 PM CDT.

VISITOR LOG

No.	Visitor	Start Time	End Time	Comments
1		05:34 PM	05:34 PM	None, while onsite.

NOTES LOG

No.	Issue?	Location	Comments
1	No	Elementary School	WTI GC/Gleason completed sidewalk replacement of the section at the Princeton Street main stairs. It is also noted that Fred M. Luth is doing work in the same area and is most likely the culprit for the loud early morning noise. Not WTI GC/Gleason.
2	No	Early Childhood Center	WTI GC/Statt -Work continues on the rubblestone wall mortar and stone removal. -The dumpster has been delivered. -MRH has placed their Bond Projects sign. WTI GC/Gleason -The area of sidewalk replacement has been marked.
3	No	Middle School & High School Projects	Field & Track Work - Bryne & Jones -Demolition work continues. -The football goal posts have been removed. -Layout and staking for concrete work in progress.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
57°F	81°F	69°F	0.00 in.	0.01 in.	0.09 in.	39%	61%	91%	54°F	3.3 mph	9 mph	18 mph


DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Clear 57°F	Clear 70°F	Partly Cloudy 75°F	Partly Cloudy 79°F	Clear 81°F	Clear 74°F

OBSERVED WEATHER CONDITIONS


No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea	Calamity
1	05:30:00 PM	No							
Comments:									

PHOTOS

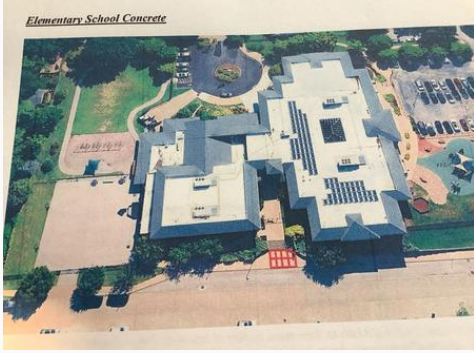

[9AEFFAB9-B574-4146-B8AC-EA0102ABB691.jpeg](#)

Area of concrete replacement at ECC today.

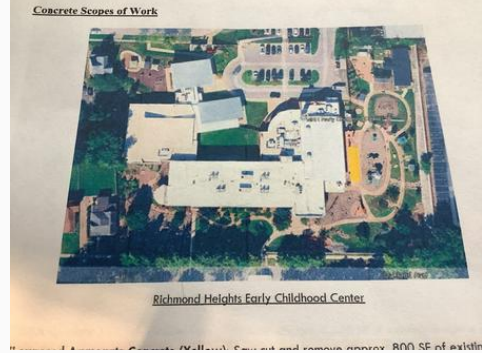

[A19EC655-3C02-4D5D-8EA9-C947B91522E6.jpeg](#)

Area (red) of concrete to be replaced at ECC.



[E95A82D5-6CF1-4DE7-99D3-CB287B38F3EE.jpeg](#)

Demo materials staged for removal. Byrne & Jones jobsite trailer moved in.



[74DBF1D9-1468-4EBF-93A8-9730285BFE01.jpeg](#)

Football goal post removed.



[42A40239-0B28-4B5B-8662-8B8A631AB543.jpeg](#)

Future Basketball Court has been staked.



[FFA94BDF-886D-4CA0-9C85-8B68530A7C07.jpeg](#)

South track crossing is in.




[71C42AAC-AC1D-4FC9-BBD0-9102824604E4.jpeg](#)

Existing disc pad has been removed.



[160B7B7F-49B7-46E2-9258-DD0164F8E762.jpeg](#)

MRH Bond Projects sign in place at ECC.

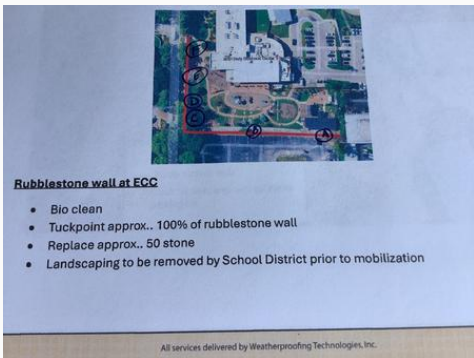

[7B074F9D-61D4-47CD-8EA5-30F633D7AC7E.jpeg](#)

ECC Rubblestone wall areas of work



[ED9086FD-10F9-4D79-81E0-A007F2533202.jpeg](#)

ECC - Removal work continues at the Rubblestone wall - Area A



[F5CA1974-3FD7-4B91-807C-5EC9C951201B.jpeg](#)

ECC - Additional Area A rubblestone wall work



[99DE5A4A-00E2-4140-912C-7D4210853598.jpeg](#)

ECC - WTI GC dumpster has been delivered.



[E52F0454-BC45-4DC2-97CC-4B8AA053E3C0.jpeg](#)

ECC - Concrete removal area has been marked.



[C38F6278-61C8-463D-91EA-71F14D620BE1.jpeg](#)

ELEM - Concrete removed and replaced at the Princeton entrance stairs.

By

Date

Copies To
