



Daily Log: Thursday 7/24/2025



Daily Log Completed

The Daily Log was completed by Ray Hutsel on Thu, Jul 24, 2025 at 01:27 PM CDT.

VISITOR LOG

No.	Visitor	Start Time	End Time	Comments
1		09:20 AM	09:20 AM	Met with Michael and the attendees from Lan Design and Bryne & Jones to review the plans and schedule for the Golf Practice Area.

NOTES LOG

No.	Issue?	Location	Comments
1	No	Elementary School	Tremco/WTI -Keeley back onsite working on replacing more concrete at the north end of the parking lot. Noted that Keeley trucks and equipment parked on the new stripe asphalt. Need to check for possible stains or damage to new asphalt after the work is done.
2	No	Early Childhood Center	Tremco/WTI (Rubblestone Wall) -Staat continues to remove existing mortar and loose stones on the Rubblestone wall. -Staat continues right behind with re-installing stones and grout the wall. -WTI reports about 50% complete overall. Tremco/WTI -Onsite today cleaning the asphalt parking lot to seal coat. Tech Electronics (Cameras) -Started installing Cat 6 cables two days ago.
3	No	Middle School & High School Projects	Bryne & Jones (Field & Track) -Met with Lan Design to review the new Golf Practice Area. -Installing new 4" sand base for the soccer field. -Shot put landing area rock installed. Daktronics (Scoreboard) -Kaemmerlen Electric/Collins & Herman have installed the new scoreboard power and low voltage underground conduits and new hand holes. Tech Electronics (Cameras) -Tech reports all cameras installed but one, and the change order work also remains to complete. Legacy (Overhand Drywall Repairs) -Not onsite today. Tremco/WTI -Bricking up the Gym window today. -Tuckpointing on the Concession stand today. -Repairing and recoating the west and bleacher concrete stairs today.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
77°F	93°F	83°F	0.00 in.	0.00 in.	0.00 in.	51%	74%	88%	74°F	4.8 mph	8 mph	16 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Clear 77°F	Partly Cloudy 85°F	Clear 92°F	Clear 96°F	Clear 95°F	Clear 88°F

OBSERVED WEATHER CONDITIONS

No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea	Calamity
1	09:15:00 AM	No							
Comments:									

PHOTOS



[8B6CB897-A2C4-420A-A275-726150BC593C.jpeg](#)

MSHS - Martini lot paving complete.




[49FBDF8C-1114-48F2-A74A-EA763B0C4CE7.jpeg](#)

MSHS - Concrete curb vs. concrete retaining wall and damaged fiber cable issues stil to be resolved.




[6507FF01-723B-462F-83D8-EB3A6EC09651.jpeg](#)

MSHS - Installing soccer field sand base today.

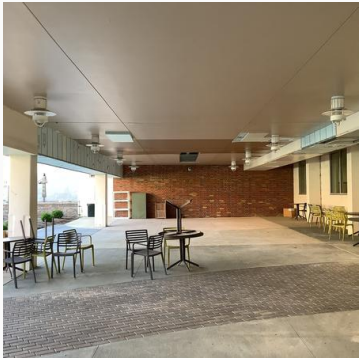

[2F80E756-9BA5-42BF-B498-648C39D5AB63.jpeg](#)

MSHS - Overhand drywall still to complete.

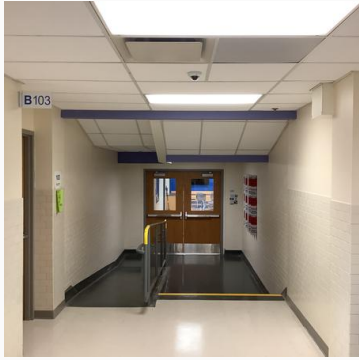

[D08D7793-43AB-431F-849A-6C1B8F218437.jpeg](#)

MSHS - New ground floor camera at entrance to the Cafe.



[43C9550F-DDD2-4EDF-9120-6246F4AD2862.jpeg](#)

MSHS - New scoreboard empty conduits to the Concession Building.



[F9D5646C-E147-48B8-B8FC-0D2BF4FB6276.jpeg](#)

MSHS - New Scoreboard power and low voltage conduits are in.



[785F7CF2-8CE1-4A01-8F66-E4FC5328A506.jpeg](#)

Placing the new soccer field sand base.



[691A91D3-FA48-4498-B798-B3FE4B566E7C.jpeg](#)

MSHS - View from the future Golf Practice Area.



[26DA7F37-FC65-484D-B220-48AC6AA25B18.jpeg](#)

MSHS - Onsite meeting today to review the Golf Practice Area.



[2765853E-3A8C-45C1-B03A-F9162D61562A.jpeg](#)

MSHS - Shot put rock landing area.



[F2B56934-0EAD-4C33-809E-508A078DCF12.jpeg](#)

MSHS - New stair coating being installed.



[6061F718-A910-467E-8343-F45FA171A885.jpeg](#)

MSHS - New concrete stair coatings being installed.



[012E0F49-D013-47FA-8B28-F203A49C77DB.jpeg](#)

MSHS - Tuckpointing ongoing at the Concession Building.



[B441AE7C-57FC-446D-B7CB-E3447D15C6F8.jpeg](#)

MSHS - Bricking up the Gym window opening.



[D8E9C865-2CA6-4137-AEC9-6CA674790447.jpeg](#)

ELEM - Replacing concrete today.



[E80ABE1E-7E76-4D54-859C-231D7DF95C79.jpeg](#)

ELEM - Trucks and equipment parked on brand new pavement.



[E195493D-4320-4303-88E3-C502BDC4E6AA.jpeg](#)

ELEM - More trucks on brand new pavement.



[5EAD42EF-E11E-49AA-8194-D519CB5D6307.jpeg](#)

ECC - Tuckpointed wall.



[EF6472A8-6744-412D-ACA8-CC8B86F77E6A.jpeg](#)

ECC - Removing grout and loose stones ahead of tuckpointers.



[C25138C0-3616-45BB-8693-C57DC07F1AA1.jpeg](#)

ECC - Statt just about to turn the corner and head south.



[BE71DD9C-98C9-4634-A6C0-CC0DB0B8DD54.jpeg](#)

ECC - Topps Paving and Sealing on the job today.



[18D49031-7DA1-49F8-A706-9DACA1CD24FB.jpeg](#)

ECC - Cleaning parking lot to seal coat.



[7308285A-9E55-407B-BC2A-F3C1C9B6A565.jpeg](#)

ECC - No entry today. Sealing the lot.

By

Date

Copies To
