



Daily Log: Wednesday 6/25/2025



Daily Log Completed

The Daily Log was completed by Ray Hutsel on Wed, Jun 25, 2025 at 11:48 AM CDT.

VISITOR LOG

No.	Visitor	Start Time	End Time	Comments
1		11:14 AM	11:14 AM	None, while onsite.

NOTES LOG

No.	Issue?	Location	Comments
1	No	Early Childhood Center	Concrete Work - Tremco/WTI -Temporary protection has been removed. -Stains from the concrete pour on adjacent areas need to be cleaned/removed.
2	No	Middle School & High School Projects	Tuckpointing (Tremco/WTI) -Grinding continues for the tuckpointing continues on the west wall. Concrete Work (Tremco/WTI) -MS & HS - Tremco/WTI preparing drawing for required ADA concrete replacement work. Field & Track Projects (Byrne & Jones) -Pouring concrete today for basketball court and javelin runway. -Potholed around the low voltage manhole. Replacement Ceiling Tile Work -Friend delivered materials and dumpster today. -Starting on removal of the rest of the ceiling tiles. -MRH has removed and salvaged good tiles for attic stock.
3	No	Early Childhood Center	Rubblestone Wall -Staat continues to remove grout at the west end of Area A. -Staat has started grouting at the west end of Area A. Burgess Concrete Work (Tremco/WTI) -Removed the temporary protection around the new concrete at the top of the Burgess stairs. -Caulking remains to complete. -Check and also clean/remove any new concrete stains. Playground Exposed Aggregate Concrete -Washing completed to expose the aggregate. -Extensive cleanup required around the new pour and down to the drain.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
78°F	89°F	81°F	0.00 in.	0.00 in.	0.00 in.	60%	76%	87%	73°F	4.6 mph	8 mph	8 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Partly Cloudy 78°F	Partly Cloudy 86°F	Partly Cloudy 93°F	Partly Cloudy 95°F	Partly Cloudy 91°F	Partly Cloudy 87°F

OBSERVED WEATHER CONDITIONS

No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea	Calamity
1	11:10:00 AM	No							
Comments:									

PHOTOS



[20DEC124-4C02-402B-B04F-2EE8F36B90D5.jpeg](#)

ELEM - Cleanup required.



[6141EBF0-1439-4271-9462-59A3079DE152.jpeg](#)

ELEM - Cleanup required.



[7D76D0AA-337D-49C0-A487-DBDFDEF0ABCE.jpeg](#)

ELEM - Cleanup required.



[22E786CB-0690-4468-9181-714218F2B948.jpeg](#)

ELEM - New concrete at Princeton entrance.



[395E9669-138F-43FB-8C39-4052D2D4E598.jpeg](#)

ECC - Asphalt work areas have been identified.



[9E50AFC2-0556-43EB-B5E5-C0F9E8B6AA88.jpeg](#)

ECC - Rubblestone wall grout materials and mixing area.



[0B8BFC03-EDF3-4264-983D-F992ED417977.jpeg](#)

ECC - Grouting started at the west end of the wall.



[869279C6-14E8-4FB0-A7B9-CBCE48CE6524.jpeg](#)

Grout and loose stone removal continues at the east end of Area A.




[9601A8D3-8BD9-4CE4-AD89-C0FA74857E25.jpeg](#)

ECC - Exposed aggregate replacement concrete area.



[3EF32A84-A45E-41CC-BABF-D999504B7A4C.jpeg](#)

ECC - Extensive cleanup from concrete work still required.

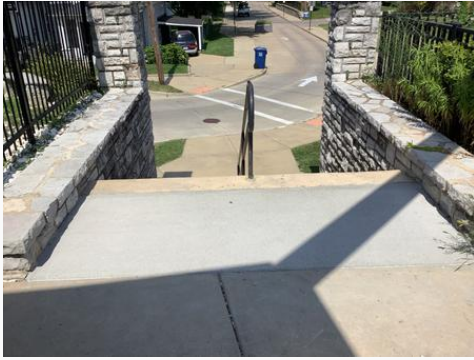

[966EA96A-94B9-402E-867B-AC37BD31F8FB.jpeg](#)

Replacment concrete at the Burgess stairs. Checking specs for caulking.



[A8653B6F-5116-4EB8-9223-927E0D962E82.jpeg](#)

Asphalt removal area has been identified. Tremco/WTI should not do this work until the concrete curb has been accepted by MRH.



[B24E5DEF-CD37-47E9-9444-8FA0341DA38F.jpeg](#)

MS_HS - Friend delivered ceiling tile materials today.



[0CF366F9-F698-473D-A3F7-679B4E57D2F8.jpeg](#)

MS-HS - Ceiling tile materials delivery truck.



[4D1BA4E1-FA0F-454B-ADB7-45FD2ADA9165.jpeg](#)

HS - Staat moving lift to work area.



[BC962042-BA27-4F9B-91C6-FBC110FA0285.jpeg](#)

HS - Staat continues to work on the west wall tuckpointing.



[62C91979-1949-4D93-9286-E2DDE1FFE7DF.jpeg](#)

MS-HS - B&J investigating around the low voltage handhole.



[3794A62B-4B52-4CFC-9D3B-4B35E7334E0C.jpeg](#)

Pouring the new javalin concrete runway today.



[4ACA43AC-83F0-419C-9260-3D91642F6EDA.jpeg](#)

B&J has hot weather cooling station and taking hot weather concrete pour precautions.



[EB649C0E-4A3F-418B-B102-3E462C4597A6.jpeg](#)

B&J checking elevation and level of the basketball pour.



[B0C9B060-E2CF-4930-8466-2CBF56F89172.jpeg](#)

Pouring the new basketball court.



[A0F67380-F552-4ED6-82F7-F9CC0AAA516F.jpeg](#)

HS - Another view of the basketball court concrete pour.



[A4F7B7AA-43CA-4BF7-94C6-588097CB0AD6.jpeg](#)

HS - Concrete wash out pit.

By

Date

Copies To
